Draft DD 10/1/22

Activity ID	Activity Name	Original Duration	Start	Finish	Calendar	Total Float
A4170	P&S - Reinforcing Steel Shop Drawings - Bridge 127 (Seg 13 & 14)	30	03-Oct-22	15-Nov-22	5x8 MA Hldys	132
A4200	R&A - Reinforcing Steel Shop Drawings - Bridge 127 (Seg 13 & 14)	20	16-Nov-22	14-Dec-22	5x8 MA Hldys	132
A4230	F&D - Prefab Truss Bridge - Bridge 127 (Seg 13 & 14)	90	01-Oct-22	29-Dec-22	7-Day	348
A5130	P&S - Steel Sheeting for Walls Shop Drawings - Bridge 127 (Seg 13 & 14)	60	03-Oct-22	29-Dec-22	5x8 MA Hldys	102
A5120	P&S - IPE Timber Rail Shop Drawings - Bridge 127 (Seg 13 & 14)	60	03-Oct-22	29-Dec-22	5x8 MA Hldys	183
A5150	R&A - Steel Sheeting for Walls Shop Drawings - Bridge 127 (Seg 13 & 14)	20	30-Dec-22	27-Jan-23	5x8 MA Hldys	102
A5140	R&A - IPE Timber Rail Shop Drawings - Bridge 127 (Seg 13 & 14)	20	30-Dec-22	27-Jan-23	5x8 MA Hldys	183
A4210	F&D - Reinforcing Steel - Bridge 127 (Seg 13 & 14)	60	15-Dec-22	12-Feb-23	7-Day	193
A4160	F&D - Steel Sheeting for Walls - Bridge 127 (Seg 13 & 14)	60	28-Jan-23	28-Mar-23	7-Day	149
A4190	F&D - IPE Timber Rail - Bridge 127 (Seg 13 & 14)	60	28-Jan-23	28-Mar-23	7-Day	265
Construction		523	03-Oct-22	30-Oct-24		-114
No Crew		20	03-Oct-22	31-Oct-22	5x8 MA Hldys (Hudson	-139
A5670	Preconstruction Storm Drain Video	3	03-Oct-22	05-Oct-22	5x8 MA Hldys (Hudson	-132
A5680	Test Pits - Hudson Roadway	10	18-Oct-22	31-Oct-22	5x8 MA Hldys (Hudson	-139
ET&L - Clearing		30	31-Oct-22	13-Dec-22		-144
No Crew		30	31-Oct-22	13-Dec-22		-144
A4780	Clearing - Segment 6 (White Pond to Sudbury TL)	2	31-Oct-22	01-Nov-22	5x8 MA Hldys (WPW &	-259
A4790	Clearing - Segment 7 (Sudbury TL to Bridge 128)	3	02-Nov-22	04-Nov-22	5x8 MA Hldys (WPW &	-252
A4800	Clearing - Segment 8 (Bridge 128 to Dutton)	1	07-Nov-22	07-Nov-22	5x8 MA Hldys (Vernal	-272
A4810	Clearing - Segment 9 (Dutton to Peakham)	3	08-Nov-22	10-Nov-22	5x8 MA Hldys (Vernal	-267
A4820	Clearing - Segment 10 (Peakham to Horse Pond)	2	14-Nov-22	15-Nov-22	5x8 MA Hldys	-326
A4830	Clearing - Segment 11 (Horse Pond to Union)	4	16-Nov-22	21-Nov-22	5x8 MA Hldys (Vernal	-262
A4840	Clearing - Segment 12 (Union to Boston Post)	1	22-Nov-22	22-Nov-22	5x8 MA Hldys	-315
A4850	Clearing - Segment 13 (Boston Post to Bridge 127)	1	23-Nov-22	23-Nov-22	5x8 MA Hldys	-314
A4860	Clearing - Segment 14 (Bridge 127 to Sudbury SS)	3	25-Nov-22	29-Nov-22	5x8 MA Hldys (Vernal	-169
A4730	Clearing - Segment 1 (Wilkins to Chestnut)	2	30-Nov-22	01-Dec-22	5x8 MA Hldys	-180
A4740	Clearing - Segment 2 (Chestnut to Bridge 130)	1	02-Dec-22	02-Dec-22	5x8 MA Hldys	-156
A4750	Clearing - Segment 3 (Bridge 130 to Main)	2	05-Dec-22	06-Dec-22	5x8 MA Hldys	-156
A4760	Clearing - Segment 4 (Main to Parmenter)	2	07-Dec-22	08-Dec-22	5x8 MA Hldys	-153
A5020	Clearing - Segment 5 (Parmenter to White Pond)	3	09-Dec-22	13-Dec-22	5x8 MA Hldys	-144
ET&L - E&S Controls		61	02-Nov-22	31-Jan-23		-171
No Crew		61	02-Nov-22	31-Jan-23		-171
A4920	E&S Controls Install - Segment 6 (White Pond to Sudbury TL)	3	02-Nov-22	04-Nov-22	5x8 MA Hldys (WPW &	-259
A4930	E&S Controls Install - Segment 7 (Sudbury TL to Bridge 128)	4	07-Nov-22	10-Nov-22	5x8 MA Hldys (WPW &	-252
A4940	E&S Controls Install - Segment 8 (Bridge 128 to Dutton)	4	14-Nov-22	17-Nov-22	5x8 MA Hldys (Vernal	-275
A4950	E&S Controls Install - Segment 9 (Dutton to Peakham)	4	18-Nov-22	23-Nov-22	5x8 MA Hldys (Vernal	-271
A4960	E&S Controls Install - Segment 10 (Peakham to Horse Pond)	4	25-Nov-22	30-Nov-22	5x8 MA Hldys	-332
A4970	E&S Controls Install - Segment 11 (Horse Pond to Union)	8	01-Dec-22	12-Dec-22	5x8 MA Hldys (Vernal	-268
A4980	E&S Controls Install - Segment 12 (Union to Boston Post)	2	13-Dec-22	14-Dec-22	5x8 MA Hldys	-328
A4990	E&S Controls Install - Segment 13 (Boston Post to Bridge 127)	2	15-Dec-22	16-Dec-22	5x8 MA Hldys	-328
A5000	E&S Controls Install - Segment 14 (Bridge 127 to Sudbury SS)	7	19-Dec-22	28-Dec-22	5x8 MA Hldys (Vernal	-182
A4870	E&S Controls Install - Segment 1 (Wilkins to Chestnut)	5	29-Dec-22	05-Jan-23	5x8 MA Hldys	-198
A4880	E&S Controls Install - Segment 2 (Chestnut to Bridge 130)	2	06-Jan-23	09-Jan-23	5x8 MA Hldys	-178
A4890	E&S Controls Install - Segment 3 (Bridge 130 to Main)	5	10-Jan-23	16-Jan-23	5x8 MA Hldys	-178
A4900	E&S Controls Install - Segment 4 (Main to Parmenter)	5	17-Jan-23	23-Jan-23	5x8 MA Hldys	-178

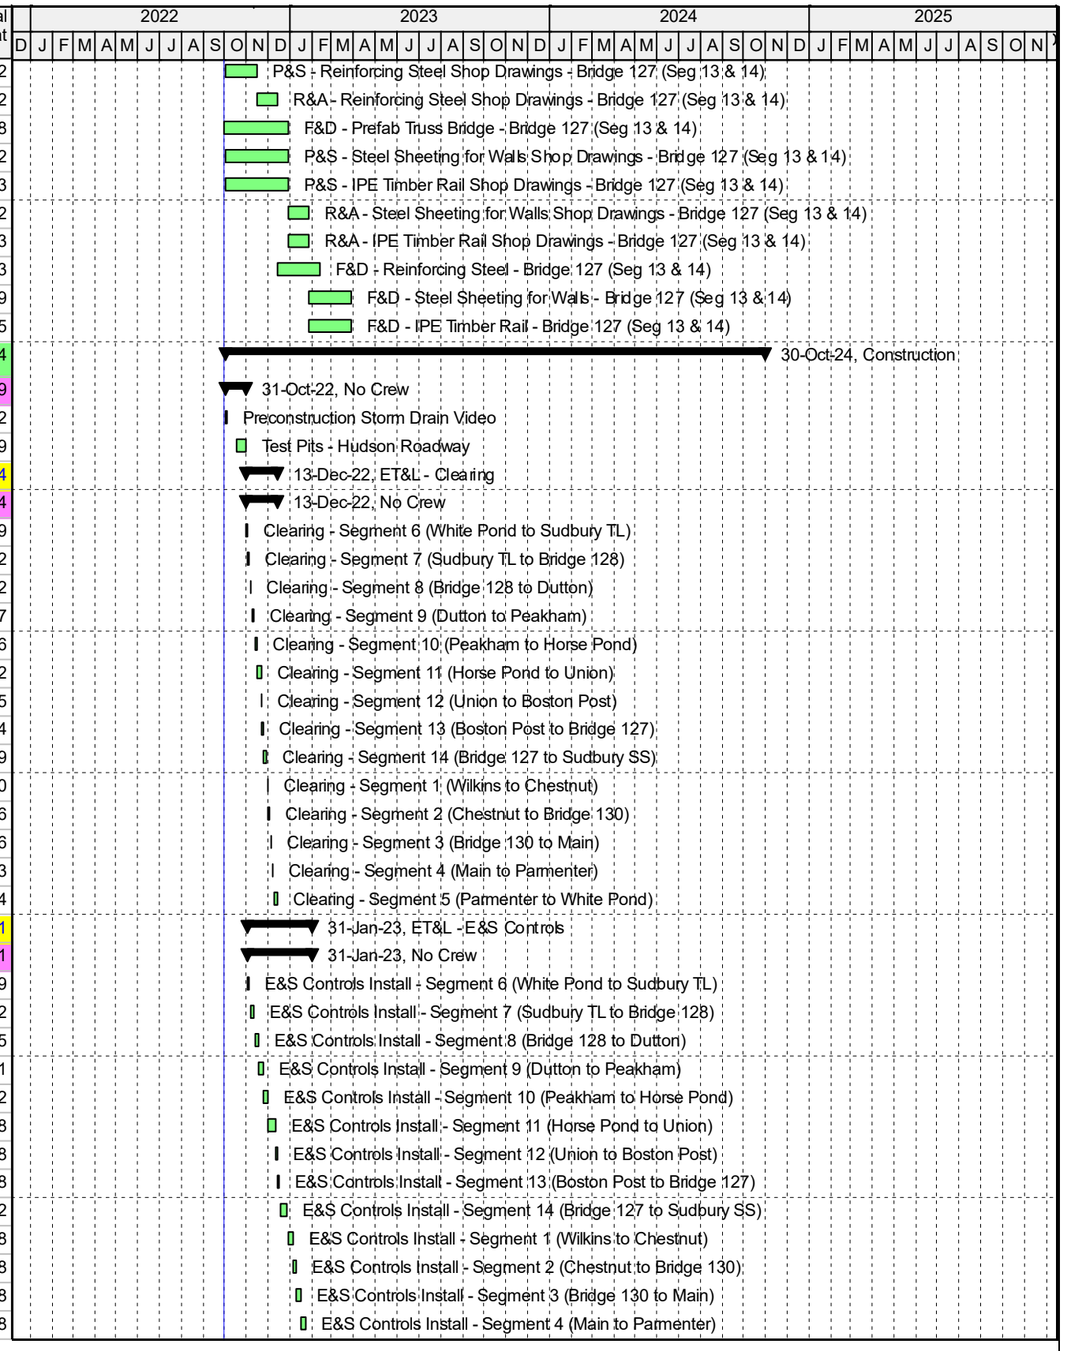

Data Date: 01-Oct-22
Finish Date: 31-May-25
Print Date: 14-Oct-22

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

BOND
Civil & Utility
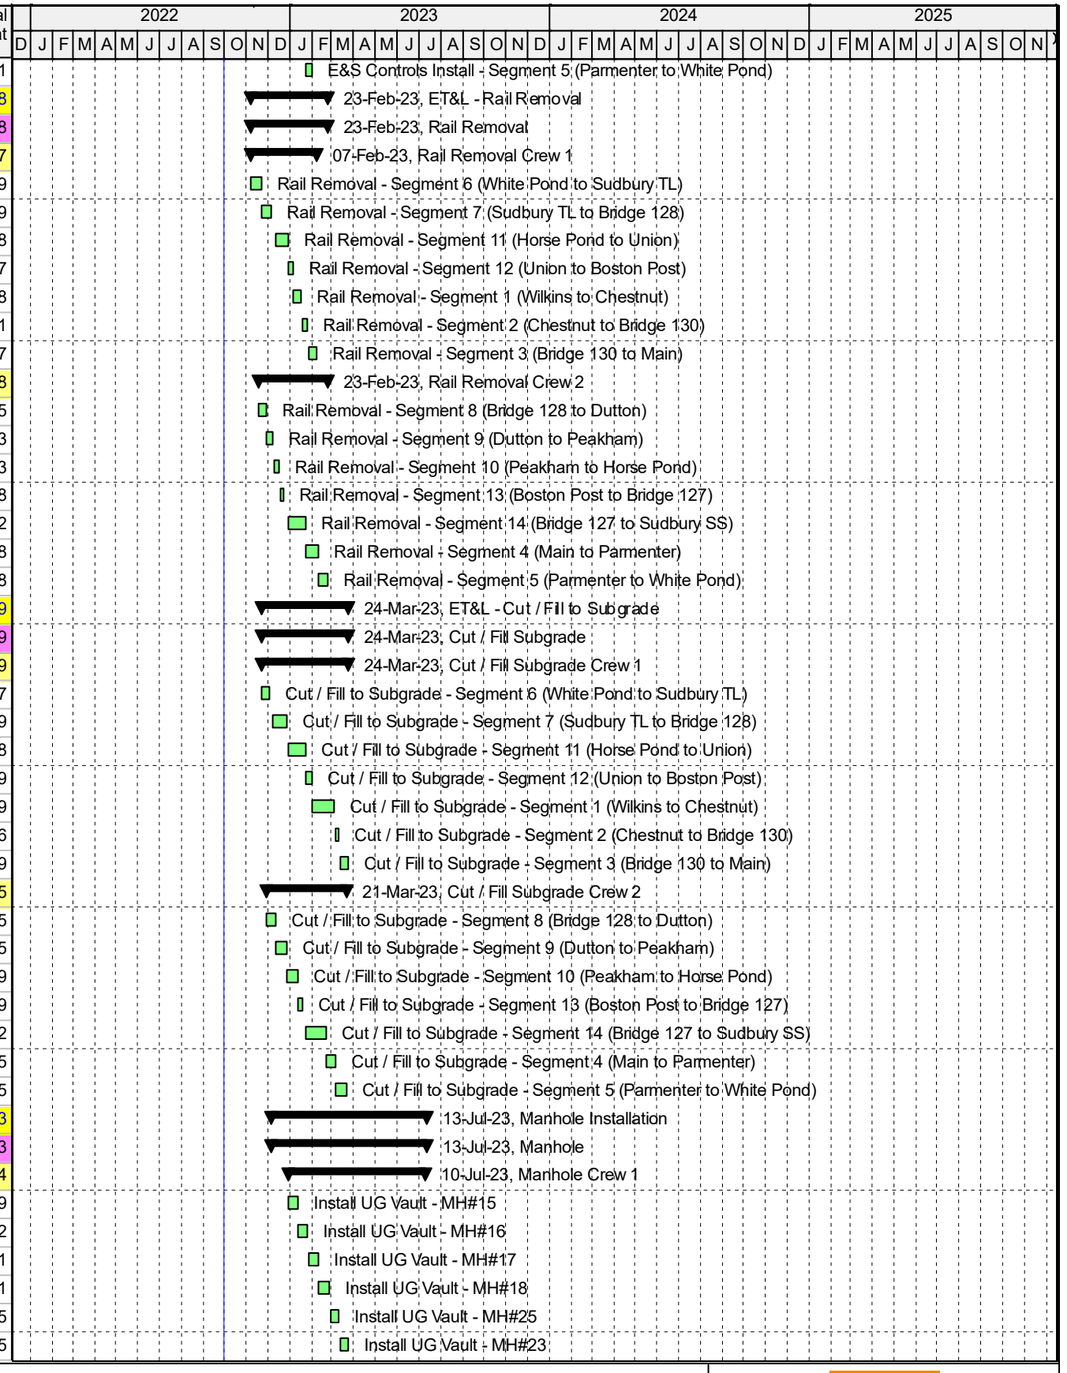
Activity ID	Activity Name	Original Duration	Start	Finish	Calendar	Total Float
A4910	E&S Controls Install - Segment 5 (Parmenter to White Pond)	6	24-Jan-23	31-Jan-23	5x8 MA Hldys	-171
ET&L - Rail Removal		74	07-Nov-22	23-Feb-23		-168
Rail Removal		74	07-Nov-22	23-Feb-23		-168
Rail Removal Crew 1		63	07-Nov-22	07-Feb-23		-157
A1220	Rail Removal - Segment 6 (White Pond to Sudbury TL)	11	07-Nov-22	22-Nov-22	5x8 MA Hldys (WPW &	-259
A1230	Rail Removal - Segment 7 (Sudbury TL to Bridge 128)	9	23-Nov-22	06-Dec-22	5x8 MA Hldys (WPW &	-259
A1270	Rail Removal - Segment 11 (Horse Pond to Union)	12	13-Dec-22	29-Dec-22	5x8 MA Hldys (Vernal	-268
A1280	Rail Removal - Segment 12 (Union to Boston Post)	4	30-Dec-22	05-Jan-23	5x8 MA Hldys	-317
A1170	Rail Removal - Segment 1 (Wilkins to Chestnut)	8	06-Jan-23	17-Jan-23	5x8 MA Hldys	-198
A1180	Rail Removal - Segment 2 (Chestnut to Bridge 130)	7	18-Jan-23	26-Jan-23	5x8 MA Hldys	-161
A1190	Rail Removal - Segment 3 (Bridge 130 to Main)	8	27-Jan-23	07-Feb-23	5x8 MA Hldys	-157
Rail Removal Crew 2		66	18-Nov-22	23-Feb-23		-178
A1240	Rail Removal - Segment 8 (Bridge 128 to Dutton)	6	18-Nov-22	28-Nov-22	5x8 MA Hldys (Vernal	-275
A1250	Rail Removal - Segment 9 (Dutton to Peakham)	8	29-Nov-22	08-Dec-22	5x8 MA Hldys (Vernal	-273
A1260	Rail Removal - Segment 10 (Peakham to Horse Pond)	6	09-Dec-22	16-Dec-22	5x8 MA Hldys	-333
A1290	Rail Removal - Segment 13 (Boston Post to Bridge 127)	5	19-Dec-22	23-Dec-22	5x8 MA Hldys	-328
A1300	Rail Removal - Segment 14 (Bridge 127 to Sudbury SS)	17	29-Dec-22	23-Jan-23	5x8 MA Hldys (Vernal	-182
A1200	Rail Removal - Segment 4 (Main to Parmenter)	13	24-Jan-23	09-Feb-23	5x8 MA Hldys	-178
A1210	Rail Removal - Segment 5 (Parmenter to White Pond)	9	10-Feb-23	23-Feb-23	5x8 MA Hldys	-178
ET&L - Cut / Fill to Subgrade		84	23-Nov-22	24-Mar-23		-179
Cut / Fill Subgrade		84	23-Nov-22	24-Mar-23		-179
Cut / Fill Subgrade Crew 1		84	23-Nov-22	24-Mar-23		-179
A1360	Cut / Fill to Subgrade - Segment 6 (White Pond to Sudbury TL)	7	23-Nov-22	02-Dec-22	5x8 MA Hldys (WPW &	-257
A1370	Cut / Fill to Subgrade - Segment 7 (Sudbury TL to Bridge 128)	15	07-Dec-22	28-Dec-22	5x8 MA Hldys (WPW &	-259
A1410	Cut / Fill to Subgrade - Segment 11 (Horse Pond to Union)	16	30-Dec-22	23-Jan-23	5x8 MA Hldys (Vernal	-268
A1420	Cut / Fill to Subgrade - Segment 12 (Union to Boston Post)	7	24-Jan-23	01-Feb-23	5x8 MA Hldys	-329
A1310	Cut / Fill to Subgrade - Segment 1 (Wilkins to Chestnut)	21	02-Feb-23	03-Mar-23	5x8 MA Hldys	-209
A1320	Cut / Fill to Subgrade - Segment 2 (Chestnut to Bridge 130)	5	06-Mar-23	10-Mar-23	5x8 MA Hldys	-186
A1330	Cut / Fill to Subgrade - Segment 3 (Bridge 130 to Main)	10	13-Mar-23	24-Mar-23	5x8 MA Hldys	-179
Cut / Fill Subgrade Crew 2		78	29-Nov-22	21-Mar-23		-185
A1380	Cut / Fill to Subgrade - Segment 8 (Bridge 128 to Dutton)	10	29-Nov-22	12-Dec-22	5x8 MA Hldys (Vernal	-275
A1390	Cut / Fill to Subgrade - Segment 9 (Dutton to Peakham)	10	13-Dec-22	27-Dec-22	5x8 MA Hldys (Vernal	-275
A1400	Cut / Fill to Subgrade - Segment 10 (Peakham to Horse Pond)	10	28-Dec-22	11-Jan-23	5x8 MA Hldys	-339
A1430	Cut / Fill to Subgrade - Segment 13 (Boston Post to Bridge 127)	5	12-Jan-23	18-Jan-23	5x8 MA Hldys	-339
A1440	Cut / Fill to Subgrade - Segment 14 (Bridge 127 to Sudbury SS)	20	24-Jan-23	21-Feb-23	5x8 MA Hldys (Vernal	-182
A1340	Cut / Fill to Subgrade - Segment 4 (Main to Parmenter)	9	22-Feb-23	06-Mar-23	5x8 MA Hldys	-185
A1350	Cut / Fill to Subgrade - Segment 5 (Parmenter to White Pond)	11	07-Mar-23	21-Mar-23	5x8 MA Hldys	-185
Manhole Installation		153	05-Dec-22	13-Jul-23		-3
Manhole		153	05-Dec-22	13-Jul-23		-3
Manhole Crew 1		133	29-Dec-22	10-Jul-23		-224
A3190	Install UG Vault - MH#15	10	29-Dec-22	12-Jan-23	5x8 MA Hldys (WPW &	-259
A3200	Install UG Vault - MH#16	10	13-Jan-23	26-Jan-23	5x8 MA Hldys (WPW)	-302
A3210	Install UG Vault - MH#17	10	27-Jan-23	09-Feb-23	5x8 MA Hldys (Vernal	-301
A3220	Install UG Vault - MH#18	10	10-Feb-23	24-Feb-23	5x8 MA Hldys (Vernal	-301
A3290	Install UG Vault - MH#25	10	27-Feb-23	10-Mar-23	5x8 MA Hldys	-365
A3270	Install UG Vault - MH#23	10	13-Mar-23	24-Mar-23	5x8 MA Hldys	-365
